


# Construction sites of SNCF - RFI - SBB for TT2025






# RFI: Focus on TCRs of the TT2025

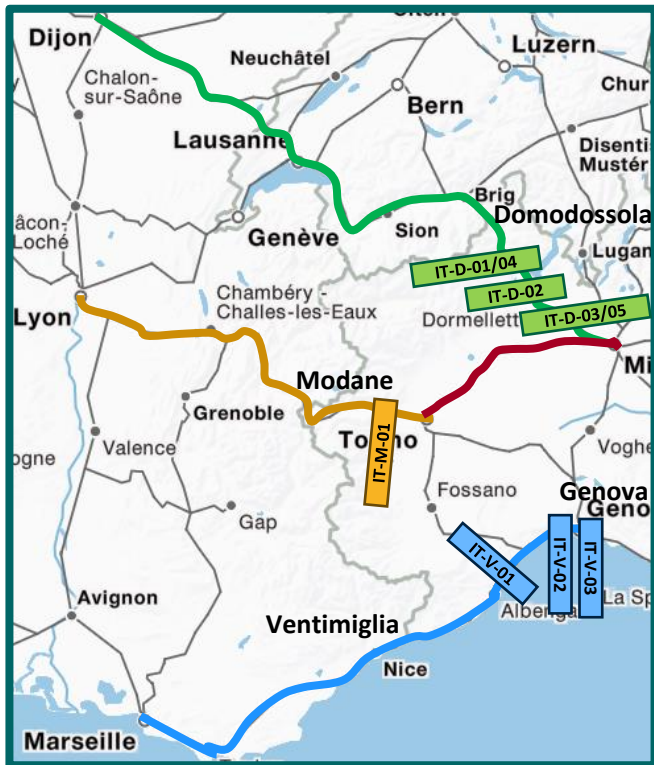


ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lione axis</b>					
IT-M-01	Bussoleno - Modane	ERTMS	Total closure: 1 x 96h 4 x 55h	29 march - 30 march 1 may - 4 may 24 may - 25 may 4 oct. - 6 oct. 8 nov. - 10 nov.	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
<b>Genova - Ventimiglia - Marsiglia axis</b>					
IT-V-01	Pietra L. - Finale L.	Maintenance bridge Bottasano	Total closure: 1 x 48h	18 jan. - 19 jan.	<b>LH:</b> limited <b>Reg:</b> limited + cancelled <b>Freight:</b> cancelled
IT-V-02	Genova Pegli	Upgrade stazione	Total closure: 1 x 48h	11 jan. - 12 jan.	<b>LH:</b> remodulation <b>Reg:</b> remodulation + limited + cancelled <b>Freight:</b> train paths remodulation
IT-V-03	Node of Genova	III Valico: activation infrastructural upgrade	Total closure: 30 days	26 july - 24 aug. (exact period to be defined)	<b>Freight:</b> cancelled with punctual reroutings via Savona - San Giuseppe (possible limitations of module and loading gauge)
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
IT-D-01	Arona - Premosello	P/C 80 + ERTMS	Total closure: 49 days + 14 days	8 june - 27 july 30 aug. - 13 sept.	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-02	Arona - Sesto Calende	Extraordinary Maintenance	Track closure	8 june - 27 july	<b>LH:</b> in shadow to IT-D-01 <b>Reg:</b> limited <b>Freight:</b> in shadow to IT-D-01
IT-D-03	Rho - Gallarate	Line upgrade + ERTMS	Total closure: 11 days	26 dec. - 6 jan. 2026	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-04	Arona - Premosello	PC 80 + ERTMS	Total closure: 3 x 72h	25 apr. - 27 apr. 3 oct. - 5 oct. 14 nov. - 16 nov.	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-05	Gallarate - Arona/Rho	ERTMS	Total closure: 9 x 31h + 1 x 96h	11-12 jan/8-9 feb/8-9 mar/ 5-6 apr/1-4 may/24-25 may/ 3-5 oct./11-12 oct/8-9 nov/ 20-21 dec	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled

# RFI: Focus on TCRs of the TT2025

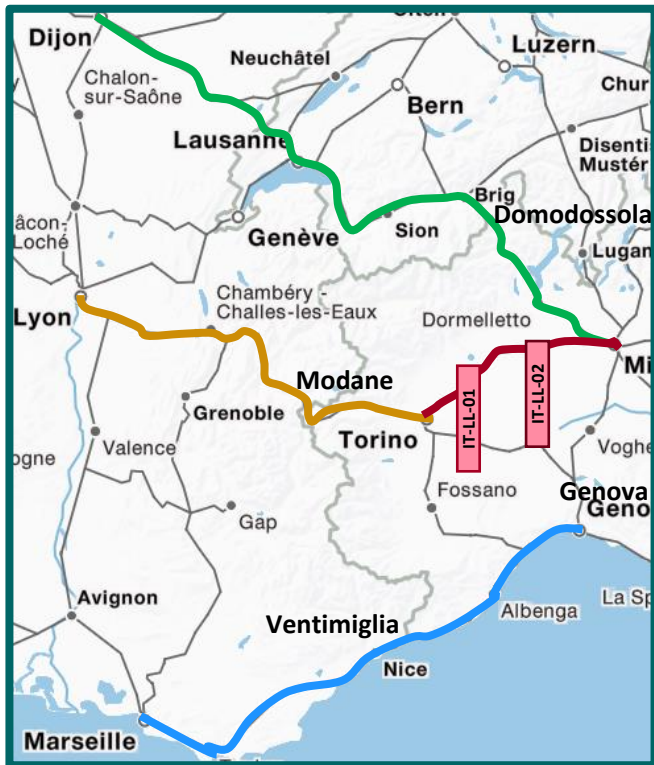

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Milano</b>					
IT-LL-01	Chivasso - Bv. Castelrosso	ERTMS	Total closure: 4 x 48h	11 jan. - 12 jan. 15 feb. - 16 feb. 8 march - 9 march 11 oct. - 12 oct.	<b>LH:</b> rerouted via Alessandria <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted via Alessandria e/o via Mortara
IT-LL-02	Trecate - Magenta	Maintenance bridge over Naviglio Grande	Total closure: 2 x 54h	15 march - 16 march 22 march - 23 march	<b>LH:</b> rerouted <b>Reg:</b> limited + cancelled <b>Freight:</b> train paths remodulation and rerouting

# SNCF Réseau: Focus on TCRs of the TT2025

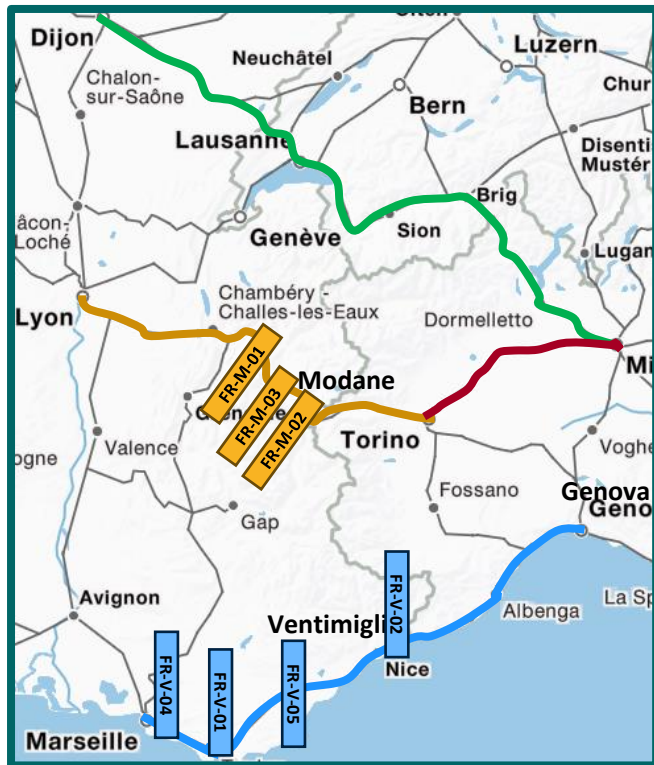

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lionne axis</b>					
FR-M-01	Montmélian - Modane	TELT Works	Periodical track closure 5h	All year	
FR-M-02	Modane	Maintenance	Total closure: 1 x 85h 1 x 64h	30 april – 04 may 08 may – 11 may	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited <b>Freight:</b> replanned + cancelled
FR-M-03	Montmélian - Modane	Tracks regeneration	Periodical day closures	All year	
<b>Genova - Ventimiglia - Marsiglia axis</b>					
FR-V-01	Toulon - La Pauline	Catenary maintenance	Periodical night 8h30 closures	2 feb. – 26 june	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-02	Antibes - Nice	Switch rails replacement	Periodical night 6h30 closures + Total closures	2 feb. – 26 june	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-03	Carnoules	<i>differed</i>			
FR-V-04	Aubagne - Cassis	Maintenance	Periodical night 7h closures	7 sept. – 11 dec.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-05	Les Arcs - Saint-Raphael	Maintenance	Periodical night 6h30 closures	29 sept. – 13 dec.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled


# Construction sites of SNCF - RFI - SBB for TT2026








# RFI: Focus on TCRs of the TT2026

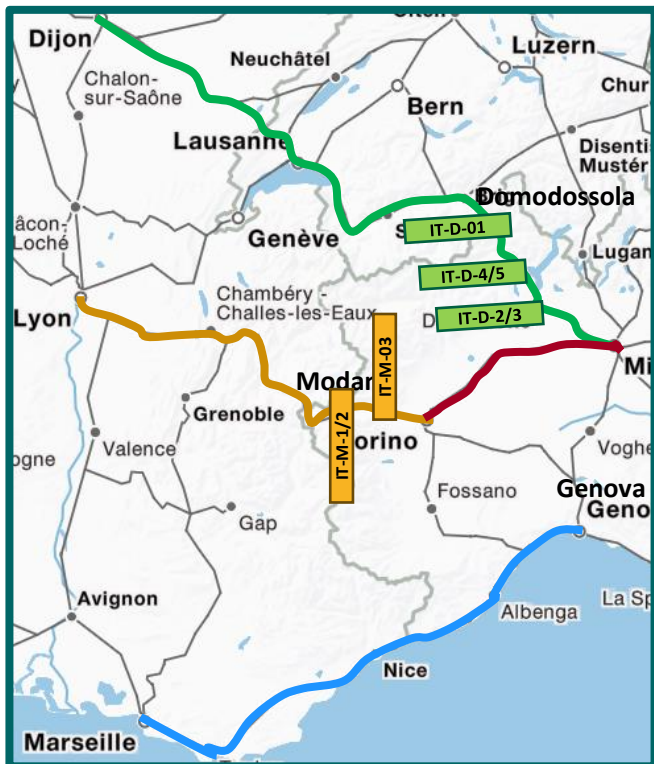

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lione axis</b>					
IT-M-01	Bussoleno - Modane	ERTMS + Maintenance	Total closure: 5 x 55h + h 1 x 72h	31 jan. - 1 feb 21 march - 22 march 11 - 12 / 18 - 19 apr. 15 may - 17 may (72h) 6 june - 7 june	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-M-02	Bussoleno - Modane	ERTMS	Total closure: 4 x 55h	11 - 13 / 18 - 20 / 25 - 27 sept. / 02 oct. - 04 oct. (in shadow to SNCF/TELT total closure)	<b>LH:</b> in shadow to SNCF/TELT <b>Reg:</b> limited + cancelled <b>Freight:</b> in shadow to SNCF/TELT
IT-M-03	Salbertrand - Chiomonte	Maintenance tunnel	Track closure: 90 days	10 aug. - 9 oct.	<b>Reg:</b> punctual limitations <b>Freight:</b> remodulation
-	Torino San Paolo	New station of Torino San Paolo SFM5	Total closure: 36h	To be defined	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> guaranteed trains with O/D Torino Orbassano + cancelled
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
IT-D-01	Iselle - Domodossola	P/C 80 + ERTMS + Line upgrade	Total closure: 60 days	29 may - 27 july	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-02	Rho - Gallarate	Line upgrade + ERTMS	Total closure: 11 + 14 days	26 dec. - 6 jan. 2026 29 may - 13 june	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-03	Gallarate - Arona/Rho	ERTMS	Total closure: 8 x 31h	24 - 25 jan. / 31 jan. - 1 feb. / 28 feb. - 1 march 21 - 22 / 28 - 29 march 11 - 12 / 18 - 19 apr. 9 may - 10 may	<b>LH:</b> cancelled <b>Reg:</b> limited <b>Freight:</b> rerouted




# RFI: Focus on TCRs of the TT2026

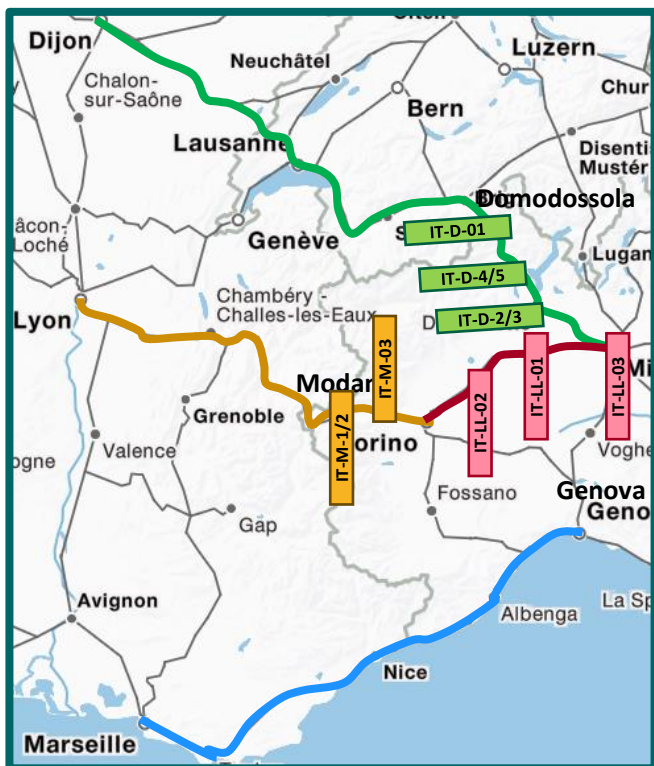


ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
IT-D-04	Arona - Premosello	P/C 80 + ERTMS	Total closure: 6x72h	27 feb. - 1 march 27 march - 29 march 18 sept. - 20 sept. 2 oct. - 4 oct. 16 oct. - 18 oct. 23 oct. - 25 oct.	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-05	Arona - Sesto Calende Sesto Calende - Oleggio	Extraordinary Maintenance	Total closure: 7 days	20 July - 27 July	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
<b>Torino - Milano</b>					
IT-LL-01	Novara Boschetto	Station improvement	Total closure: 23 days	4 July - 27 July	<b>Freight:</b> cancelled
IT-LL-02	Chivasso - Bv. Castelrosso	ERTMS	Total closure: 6 x 48h + 2 x 48h (exact period to be defined)	17 Jan. - 18 Jan. 24 Jan. - 25 Jan. 28 Feb. - 1 March 28 March - 29 March 23 May - 24 May 30 May - 31 May	<b>LH:</b> rerouted via Alessandria <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted via Alessandria e/o via Mortara
IT-LL-03	Milano Porta Garibaldi	Technological upgrade: ACC	Track interruption in different phases for 71 days	4 apr. - 13 June	<b>LH:</b> elimination of services in the Milan P. Garibaldi station and suppression of the Milan P. Garibaldi stop <b>Reg:</b> limited + cancelled

# SNCF Réseau: Focus on TCRs of the TT2026

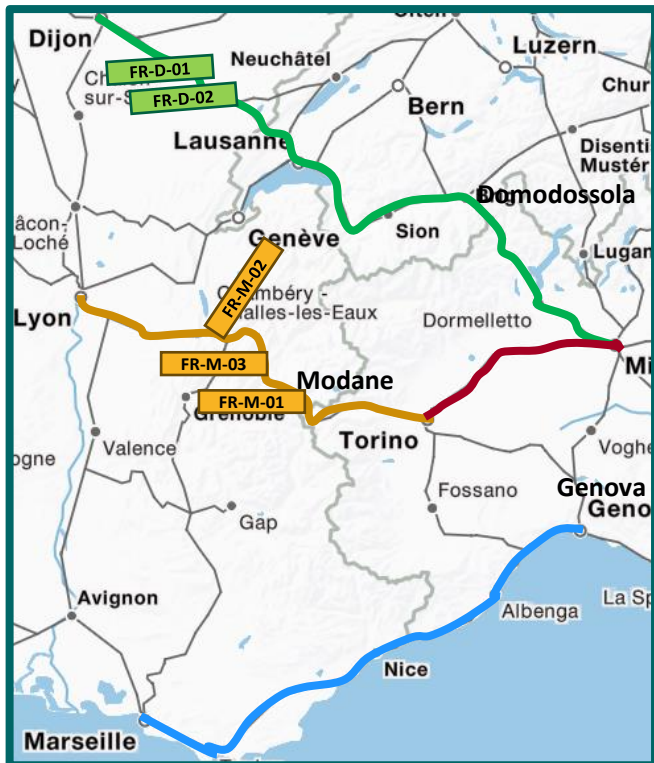

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lione axis</b>					
FR-M-01	Montmélian – Modane	TELT Works	Total Closure 28 days + Periodical 6h closures (day + night to be confirmed)	11 sept – 09 oct. + 05 jan. – 11 dec.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-M-02	Montmélian – St-Pierre-d’Albigny	RVB	Periodical closure: 6 to 8 hours (night to be confirmed)	6 jul. – 2 oct.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited <b>Freight:</b> replanned + cancelled
FR-M-03	St-Pierre-d’Albigny – Modane	RVB + Madeleine Tunnel	Periodical closure: 6 to 8 hours (day + night to be confirmed)	15 jun. – 10 sept.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited <b>Freight:</b> replanned + cancelled
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
FR-D-01	Mouchard	Switch rails and tracks replacement	Total closure 2 x 34h 1 x 14h + Periodical closure	14/15 march 28/29 march 12/13 june + 13 jan. – 10.jul.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-D-02	Andelot	maintenance	Periodical 7h night closure	13 jan. – 10 jul.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled

# SNCF Réseau: Focus on TCRs of the TT2026

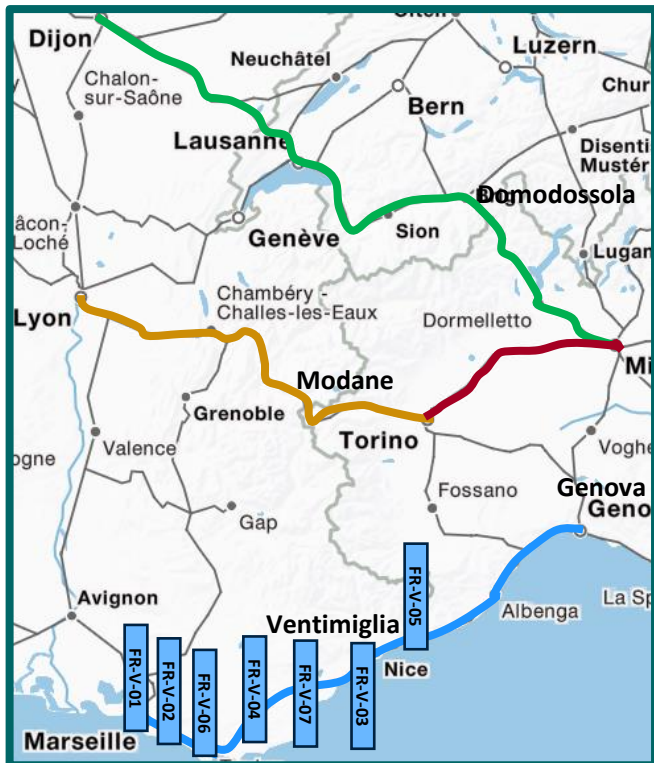

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Genova - Ventimiglia - Marsiglia axis</b>					
FR-V-01	Marseille-Vintimille	Rail bridge maintenance	Total closure 1 x 157 h 1 x 36 h	8 nov. – 15 jun. 18 sept. – 20 sept.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-02	Marseille	Switch rails replacement	Total closures 1 x 60h 1 x 54h 1 x 35 h	14->17 may 23->25 may 30->31 may	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-03	Frejus - Nice	Maintenance	Periodical night 7h closures	26 jan. – 16 apr.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-04	Toulon – Les Arcs	Catenary maintenance	Periodical night 6 to 8h closures	11 oct. – 10 dec.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-05	Nice - Vintimille	Rail bridge maintenance	Total Closure 1 x 96h Periodical night 8h closures	8->12oct. 30 aug. – 30 nov.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> replanned + cancelled
FR-V-06	Aubagne - Toulon	maintenance	Periodical night 6hclosures	5 jan – 21 may	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited <b>Freight:</b> replanned + cancelled
FR-V-07	Marseille - Vintimille	HPMV	Periodical night 6h closures	5 jan. – 10 jul.	<b>LH:</b> replanned + cancelled <b>Reg:</b> limited <b>Freight:</b> replanned + cancelled

# Major Construction sites of SNCF - RFI - SBB for TT2027


# Construction sites of SNCF - RFI - SBB for TT2027




		January 27	February 27	March 27	April 27	May 27	June 27	July 27	August 27	September 27	October 27	November 27	December 27																																									
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	#
ID	SECTION, REASON FOR ACTIVITY																																																					
<b>Torino - Modane - Lione axis</b>																																																						
IT-M-01	BUSSOLENO - MEANA, MAINTENANCE TUNNEL																																																					
IT-M-02	SALBERTRAND - MEANA, TRACK RENEWAL																																																					
FR-M-01	Montmélian-St Pierre D'albiny, TVP																																																					
FR-M-02	ST AVRE- ST JEAN, TELT																																																					
FR-M-04	St Jean- Modane, OA 224																																																					
<b>Genova - Ventimiglia - Marsiglia axis</b>																																																						
FR-V-01	Marsiglia-Vintimiglia, Divers travaux mod																																																					
FR-V-03	Marsiglia-Vintimiglia, Divers travaux mod																																																					
FR-V-03	Marsiglia-Vintimiglia, Divers travaux mod																																																					
FR-V-04	Nice-Vintimiglia, TX OA Miron																																																					
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>																																																						
IT-D-01	ISELLE - DOMODOSSOLA, P/C 80*																																																					
IT-D-02	DOMODOSSOLA - BV. VALLE, P/C 80*																																																					
FR-D-01	MOUCHARD-ANDELOT, Poste du Jura																																																					
FR-D-02	ANTELLOT-FRASNE, Tu Moringon																																																					
FR-D-03	FRASNE VALLORBE, Tu Mt d'Or																																																					
CH-D-01	GALLERIA DEL SEMPIONE, sbarramento di 1/4																																																					
CH-D-02	Vevey, Rinnovo binario, sbarramento totale																																																					
Ulteriori singole notti di sbarramenti totali tutto																																																						

**Legend:**

- Line closure
- Track closure
- Periodical total closure at night
- Periodical daytime total closure

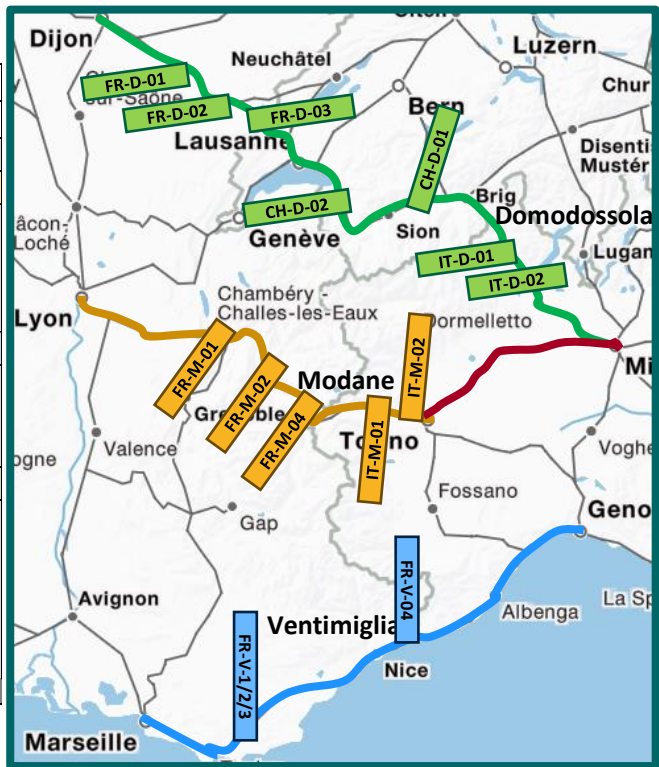


# RFI: Focus on TCRs of the TT2027

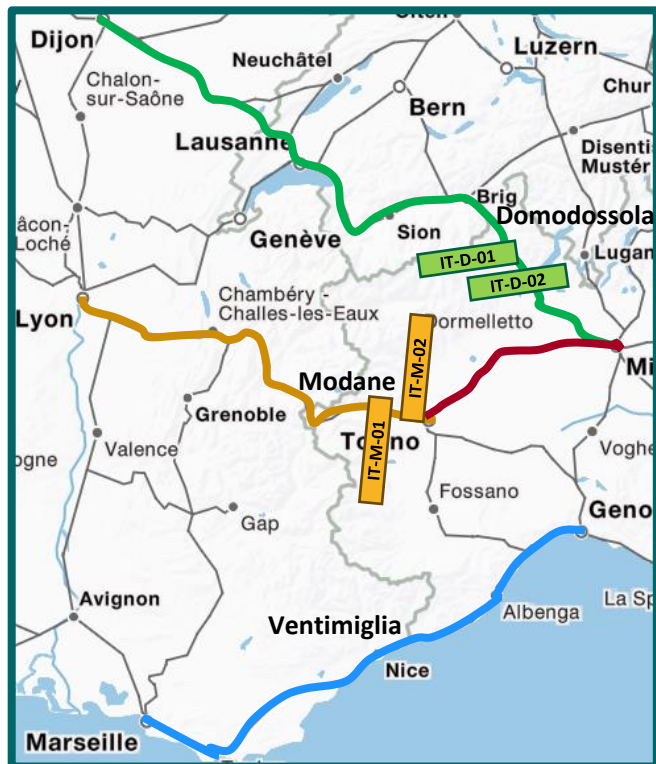

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lione axis</b>					
IT-M-01	Bussoleno - Meana	Maintenance tunnel	Track closure: 40 days	13 june - 23 july	<b>Reg:</b> punctual limitations <b>Freight:</b> train paths remodulation
IT-M-02	Salbertrand - Meana	Track renewal	Track closure: 50 days	24 july - 12 sept.	<b>Reg:</b> punctual limitations <b>Freight:</b> train paths remodulation
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
IT-D-01	Iselle - Domodossola	P/C 80	Track closure: 40 days	10 may - 18 june (in the same period with DB InfraGO closure)	<b>LH:</b> punctual train paths remodulation <b>Reg:</b> punctual train paths remodulation and limitations <b>Freight:</b> reroutings and punctual train paths remodulation
IT-D-01	Iselle - Domodossola	P/C 80	Total closure: 21 days	19 june - 9 july (in the same period with DB InfraGO closure)	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled
IT-D-02	Domodossola - Bv. Valle	P/C 80	Track closure: 40 days	19 june - 28 july	<i>From 9 july to 28 july (outside the total closure)</i> <b>LH:</b> punctual train paths remodulation <b>Reg:</b> punctual train paths remodulation and limitations <b>Freight:</b> reroutings and punctual train paths remodulation
-	Rho - Gallarate	Line upgrade	Total closure: 28 days	jan. - dec. <i>Period being defined</i>	<b>LH:</b> cancelled <b>Reg:</b> limited + cancelled <b>Freight:</b> rerouted + cancelled



# SNCF Réseau: Focus on TCRs of the TT2027

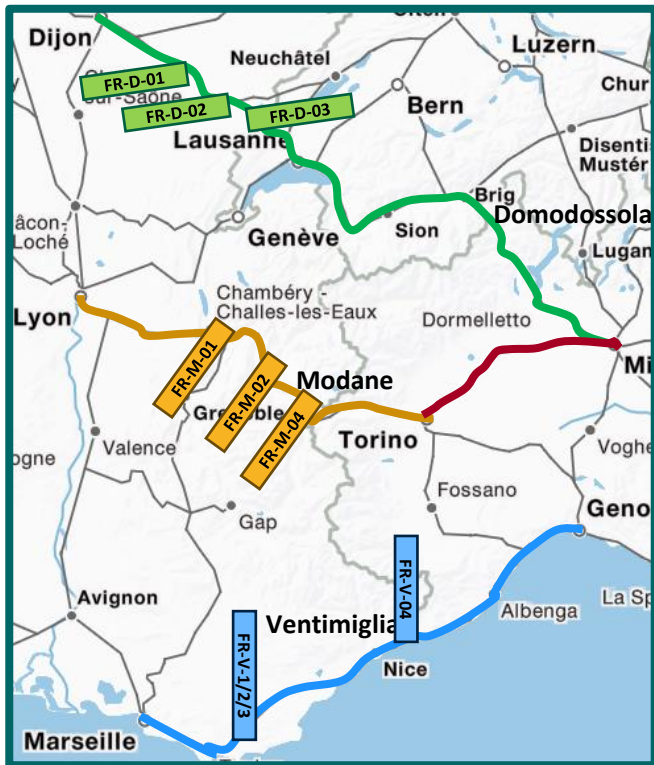

ID TCR	Section	Activity	Impact of TCR	Period	Traffic measures
<b>Torino - Modane - Lione axis</b>					
FR-M-01	Montmélian – St-Pierre-d’Albigny	TVP	Total Closure 1 WE Periodical closure	WE 19/20 W3 -> W27	To be evaluated
FR-M-02	St-Avre – St-Jean	TELT works	Total Closure 1 WE Periodical closure	WE 12/13 All year	To be evaluated
FR-M-03	St-Jean - Modane	maintenance	Total Closure 1 WE Periodical closure	WE 12/13 W11 -> W18	To be evaluated
<b>Genova - Ventimiglia - Marsiglia axis</b>					
FR-V-01 FR-V-02 FR-V-03	Marseille - Vintimille	Development & maintenance	Total Closure 14 WE + Periodical closure	7 WE on S1 5 WE on S2 All year	To be evaluated
FR-V-04	Nice Vintimille	maintenance	Total Closure 2 weeks	W45 -> W46	To be evaluated
<b>Milano - Domodossola - Vallorbe - Dijon axis</b>					
FR-D-01	Mouchard - Andelot	maintenance	Total Closure 1 WE Periodical closure	WE 12/13 W12 -> W17	To be evaluated
FR-D-02	Andelot - Frasne	maintenance	Periodical closure	W8 -> W43	To be evaluated
FR-D-03	Frasne – Vallorbe	maintenance	Periodical closure	W11 -> W43	To be evaluated
